

Quantitative Project Management

MGT 207

10/8/26

Idea Behind Formalizing PM

- Learn the “Physics” of Project Management

Idea Behind Formalizing PM

- **Learn the “Physics” of Project Management**

- The goal of learning these mathematical models (CPM, PERT) isn't just to help you win today's simulation game.

Idea Behind Formalizing PM

- **Learn the “Physics” of Project Management**

- The goal of learning these mathematical models (CPM, PERT) isn't just to help you win today's simulation game.
- It is to teach you the underlying mechanics of how projects behave. Without understanding these foundational physics, it is very hard to manage complex projects competently without resorting to superficial guesswork.

Idea Behind Formalizing PM

- **Learn the “Physics” of Project Management**

- The goal of learning these mathematical models (CPM, PERT) isn't just to help you win today's simulation game.
- It is to teach you the underlying mechanics of how projects behave. Without understanding these foundational physics, it is very hard to manage complex projects competently without resorting to superficial guesswork.

- **Use structure to combat scale and complexity**

Idea Behind Formalizing PM

- **Learn the “Physics” of Project Management**

- The goal of learning these mathematical models (CPM, PERT) isn't just to help you win today's simulation game.
- It is to teach you the underlying mechanics of how projects behave. Without understanding these foundational physics, it is very hard to manage complex projects competently without resorting to superficial guesswork.

- **Use structure to combat scale and complexity**

- **Make future possibilities more predictable**, foresee problems, develop contingency plans

Idea Behind Formalizing PM

- **Learn the “Physics” of Project Management**

- The goal of learning these mathematical models (CPM, PERT) isn't just to help you win today's simulation game.
- It is to teach you the underlying mechanics of how projects behave. Without understanding these foundational physics, it is very hard to manage complex projects competently without resorting to superficial guesswork.

- **Use structure to combat scale and complexity**

- **Make future possibilities more predictable**, foresee problems, develop contingency plans

- **Forces us to confront things that are hard to think about in detail**

Idea Behind Formalizing PM

- **Learn the “Physics” of Project Management**

- The goal of learning these mathematical models (CPM, PERT) isn't just to help you win today's simulation game.
- It is to teach you the underlying mechanics of how projects behave. Without understanding these foundational physics, it is very hard to manage complex projects competently without resorting to superficial guesswork.

- **Use structure to combat scale and complexity**

- **Make future possibilities more predictable**, foresee problems, develop contingency plans

- **Forces us to confront things that are hard to think about in detail**

- Helpful even when the details don't unfold as expected

Idea Behind Formalizing PM

- **Learn the “Physics” of Project Management**

- The goal of learning these mathematical models (CPM, PERT) isn't just to help you win today's simulation game.
- It is to teach you the underlying mechanics of how projects behave. Without understanding these foundational physics, it is very hard to manage complex projects competently without resorting to superficial guesswork.

- **Use structure to combat scale and complexity**

- **Make future possibilities more predictable**, foresee problems, develop contingency plans

- **Forces us to confront things that are hard to think about in detail**

- Helpful even when the details don't unfold as expected
- Eisenhower: “The plan is nothing. Planning is everything.”

Setting Up Project Norms

- **Determine how the project will operate day to day**

Setting Up Project Norms

- **Determine how the project will operate day to day**
 - Set norms for meetings, updates, communication

Setting Up Project Norms

- **Determine how the project will operate day to day**
 - Set norms for meetings, updates, communication
 - Establish official processes for logging, reviewing, updating progress on issues

Setting Up Project Norms

- **Determine how the project will operate day to day**
 - Set norms for meetings, updates, communication
 - Establish official processes for logging, reviewing, updating progress on issues
 - Set norms and escalation procedures for disagreements and unresolved issues

Setting Up Project Norms

- **Determine how the project will operate day to day**
 - Set norms for meetings, updates, communication
 - Establish official processes for logging, reviewing, updating progress on issues
 - Set norms and escalation procedures for disagreements and unresolved issues
- **Important questions:**

Setting Up Project Norms

- **Determine how the project will operate day to day**
 - Set norms for meetings, updates, communication
 - Establish official processes for logging, reviewing, updating progress on issues
 - Set norms and escalation procedures for disagreements and unresolved issues
- **Important questions:**
 - What do we do when we encounter a new problem?

Setting Up Project Norms

- **Determine how the project will operate day to day**
 - Set norms for meetings, updates, communication
 - Establish official processes for logging, reviewing, updating progress on issues
 - Set norms and escalation procedures for disagreements and unresolved issues
- **Important questions:**
 - What do we do when we encounter a new problem?
 - Who do we go to for help making decisions?

Setting Up Project Norms

- **Determine how the project will operate day to day**
 - Set norms for meetings, updates, communication
 - Establish official processes for logging, reviewing, updating progress on issues
 - Set norms and escalation procedures for disagreements and unresolved issues
- **Important questions:**
 - What do we do when we encounter a new problem?
 - Who do we go to for help making decisions?
 - How do we check progress on a known issue?

Overview

- I. Project scheduling with known activity times**
 - Example
 - CPM approach
- II. Project Crashing**
 - Heuristic approach
- III. Project scheduling with uncertain activity times**
 - PERT approach
 - Simulation approach
- IV. Case study discussion**

Product Launch at AeroTech Solutions

AeroTech Solutions has designed a revolutionary new autonomous delivery drone targeted at commercial logistics companies. R&D and core design are complete. All that remains is to plan the manufacturing ramp-up and the global marketing campaign. The company has identified 9 key activities and the estimated costs for the project launch. How should AeroTech schedule these activities to hit the market in the shortest possible time?

Activity	Activity Description	Immediate Predecessor	Activity Time (weeks)	Normal Cost
A	Conduct market analysis	—	6	\$240,000
B	Secure manufacturing facilities	A	4	\$300,000
C	Hire production managers	A	3	\$150,000
D	Procure raw materials	B	3	\$540,000
E	Hire & train assembly team	B, C	10	\$900,000
F	Manufacture pilot units (prototypes)	D, E	2	\$300,000
G	Scale to full production	F	6	\$1,350,000
H	Develop marketing strategy	B	6	\$450,000
I	Execute global launch campaign	H, F	8	\$1,050,000
Total			48	

Construction of a Network Diagram

Given:

- ① list of all activities
- ② precedence relationships
- ③ estimates of time and cost for each activity

We are able to construct a network diagram where:

- ① each node represents an activity
- ② each arc represents the precedence relationship between two activities
- ③ there is a (dummy) starting node ST and a (dummy) finishing node FIN

Scheduling Calculations

After creating a network of a project, the next step in the CPM is to determine the earliest time that each activity in the network can start and finish. We determine these by what is called a **forward pass**.

A. Notation

- t_k = estimate of the mean duration time of activity k
- ES_k = **earliest start** time for activity k
- EF_k = **earliest finish** time for activity k
- LS_k = **latest allowable start** time for activity k
- LF_k = **latest allowable finish** time for activity k

ES_k	EF_k
k	t_k
LS_k	LF_k

Forward Pass

B. Rules

(1) Forward Pass (ES, EF)

Step 1: for START node, set $ES_{start} = 0$

Step 2: an arbitrary activity k is assumed to start as soon as all of its predecessor activities are completed. This may be written as:


$$ES_k = \text{largest EF of activity } k\text{'s predecessors} = \max_{j \in k\text{'s immed. pred.}} \{EF_j\}$$

= the earliest possible time to start activity k


Step 3: the earliest possible finish time of activity k is the sum of its earliest start time and the estimated activity time.

$$EF_k = ES_k + t_k$$


Forward Pass (Step-by-Step)

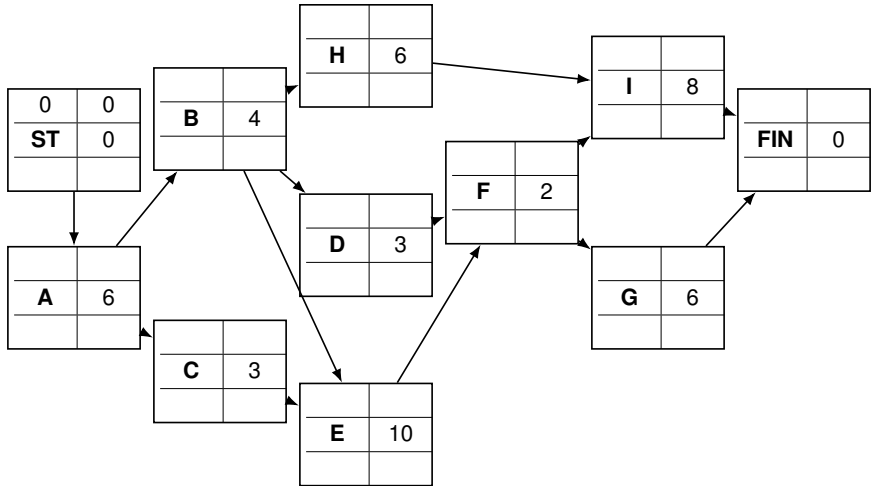


Forward Pass (Step-by-Step)

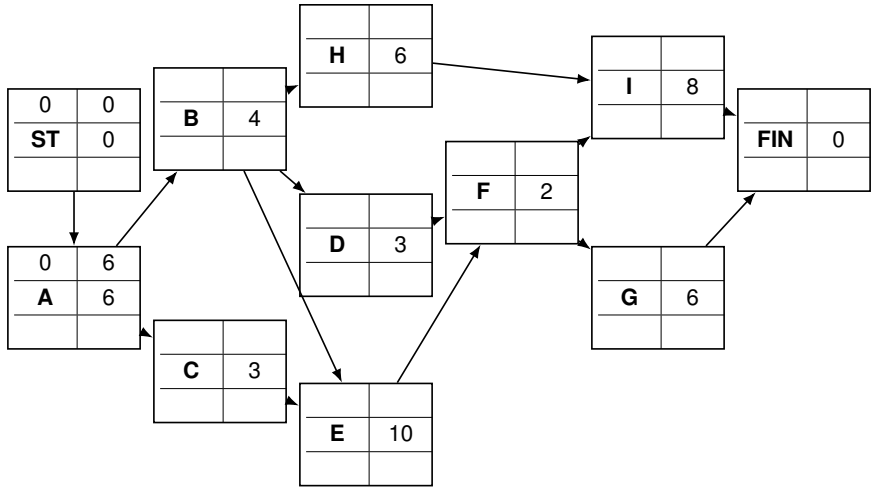


Forward Pass (Step-by-Step)

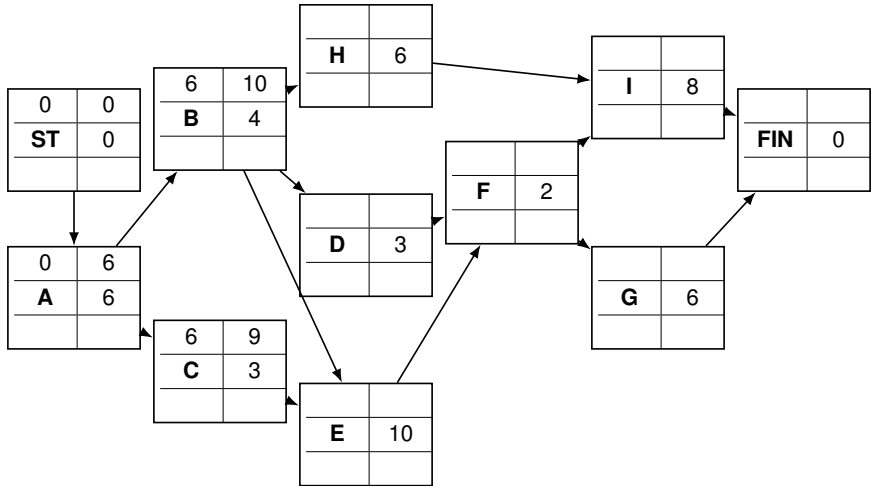


Forward Pass (Step-by-Step)

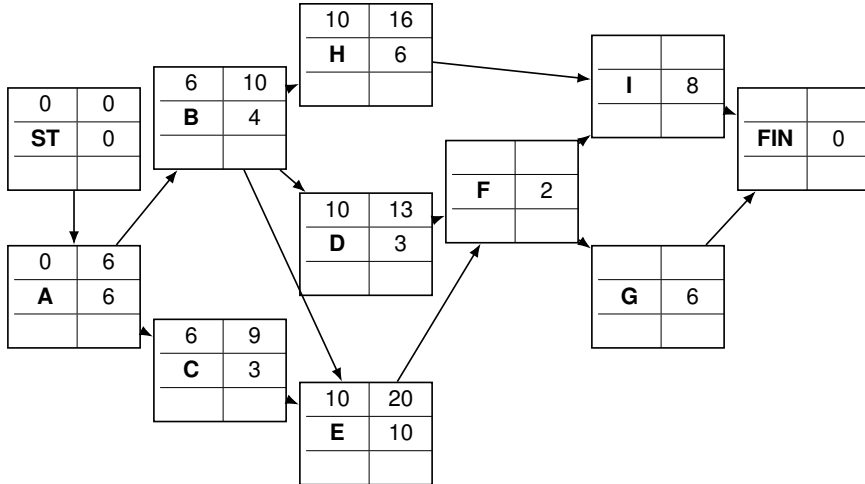


Forward Pass (Step-by-Step)

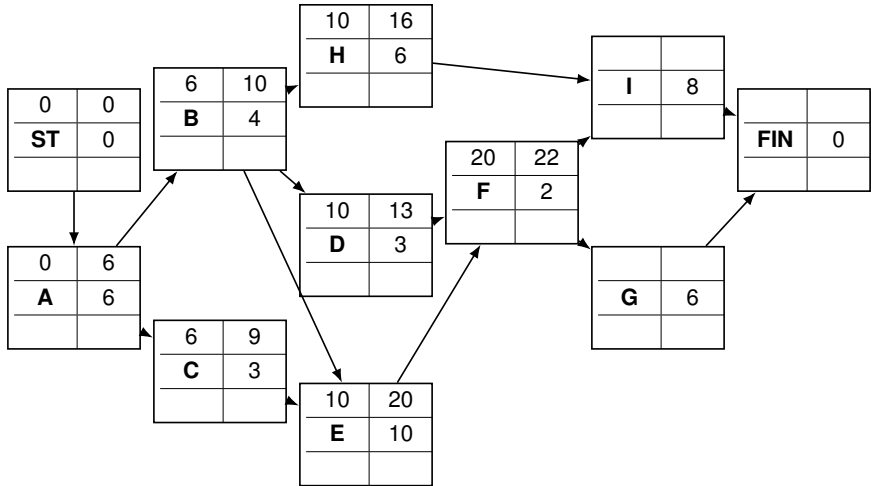

Forward Pass (Step-by-Step)

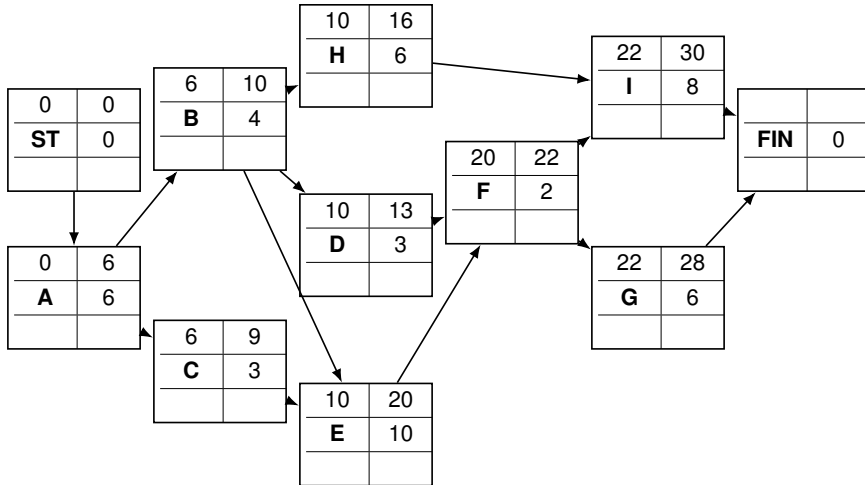

Forward Pass (Step-by-Step)

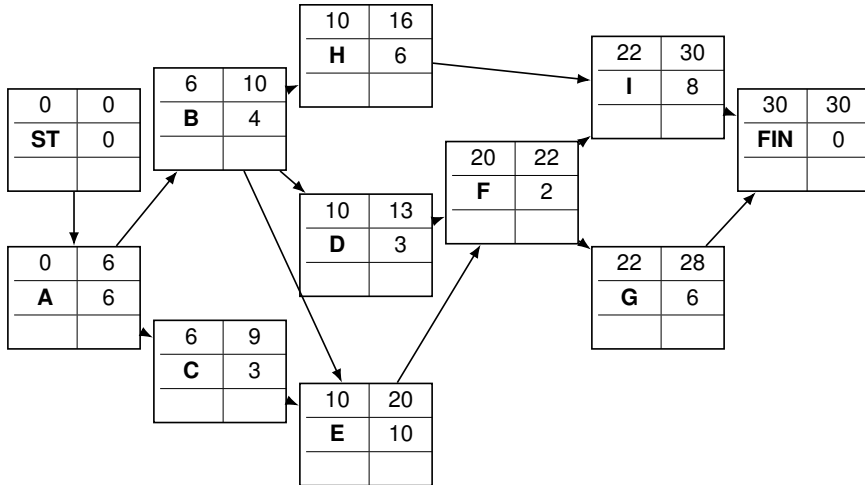

Backward Pass

(2) Backward Pass (LS, LF)

Step 1: LF of FINISH node is set equal to its earliest finish time as computed in the forward pass computations: $LF_{FIN} = EF_{FIN}$

Step 2: the latest allowable finish time for activity k without delaying the entire project is the smallest (or earliest) of the latest allowable start times of its successor activities.


$$LF_k = \text{smallest LS of } k\text{'s successors} = \min_{j \in k\text{'s immed. succ.}} \{LS_j\}$$

= latest allowable finish time for activity k without affecting proj. completion


Step 3: the latest allowable start time for activity k without delaying the entire project is its latest allowable finish time minus the estimated activity time.

$$LS_k = LF_k - t_k$$


Backward Pass (Step-by-Step)

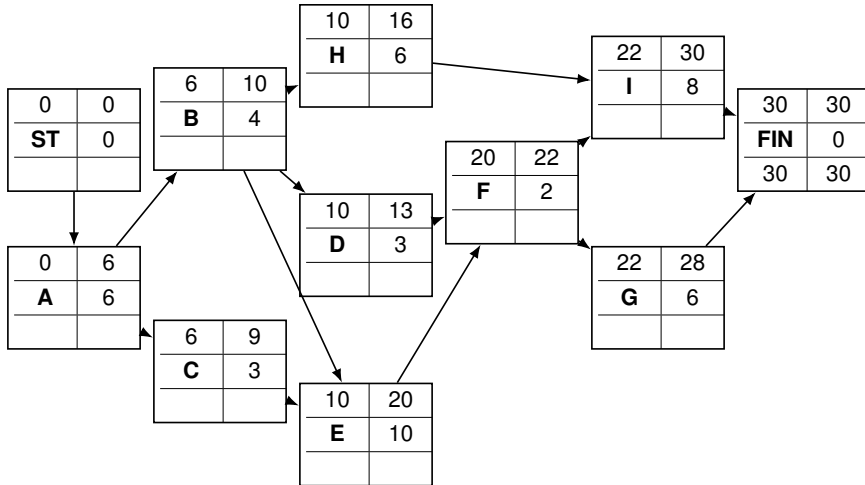


Backward Pass (Step-by-Step)

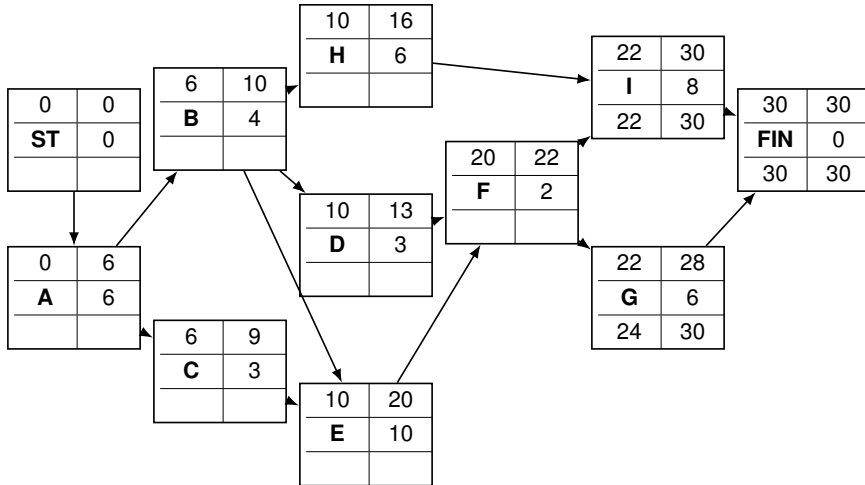


Backward Pass (Step-by-Step)

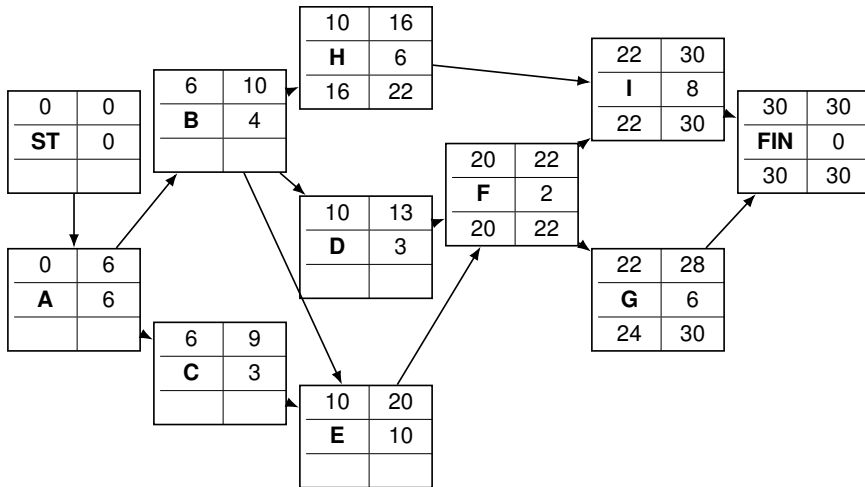


Backward Pass (Step-by-Step)

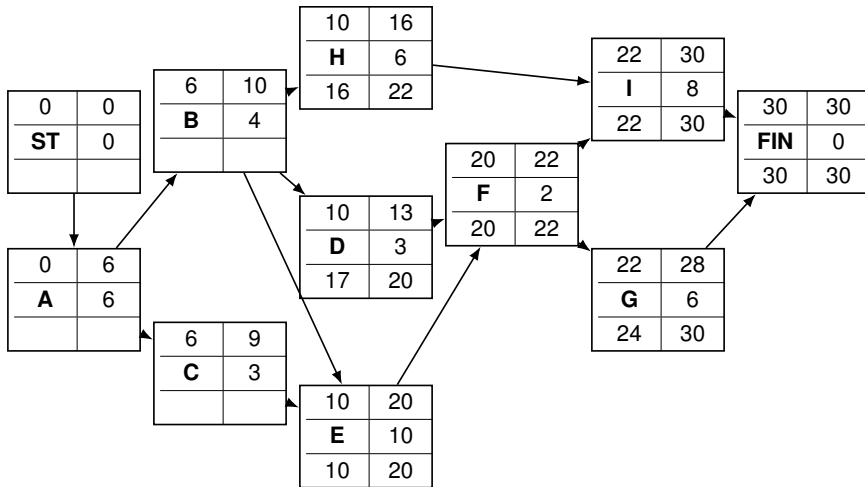

Backward Pass (Step-by-Step)

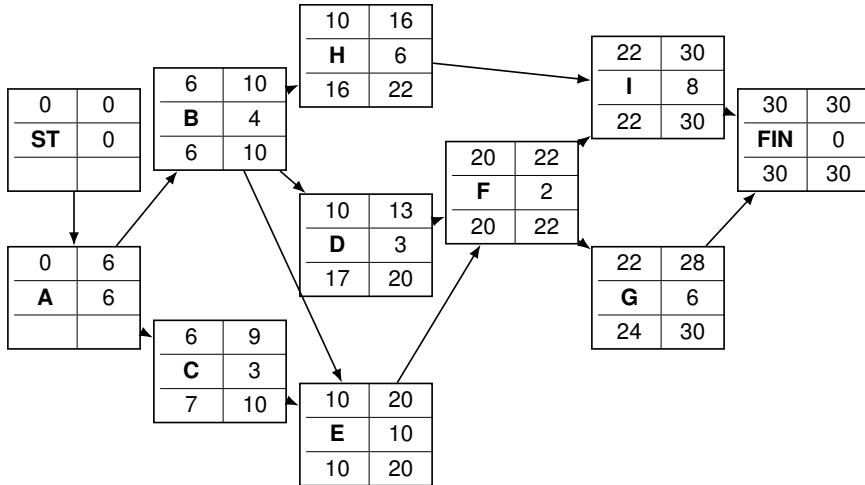

Backward Pass (Step-by-Step)

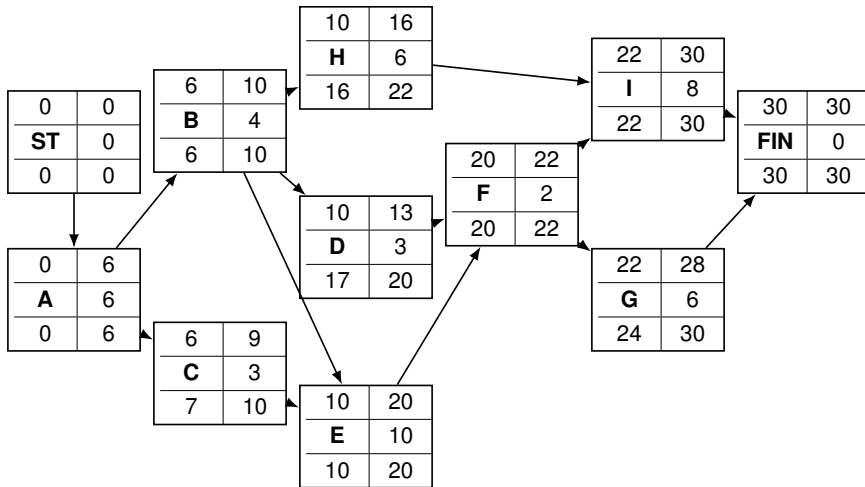

After Backward Pass: Slack

We know:

- The latest allowable starting time and the latest allowable finishing time for each activity

So... Define Slack:

$$SLACK_k = LS_k - ES_k = LF_k - EF_k$$

= the length of time an activity can be delayed without affecting the completion date for the entire project, assuming all its immediate predecessors start at ES.

i.e., activity k can be delayed by $SLACK_k$ from its ES_k without affecting the project completion time.

Connection to Simulation

Speeding up a task with positive slack (e.g., by adding resources or overtime) **wastes budget without shortening the overall project schedule**. You must identify the Critical Path first!

Critical Path

- **Path**

Critical Path

- **Path**

- A sequence of connected activities that leads from the START node to the FINISH node.

Critical Path

- **Path**

- A sequence of connected activities that leads from the START node to the FINISH node.

- **Critical Path (CP)**

Critical Path

- **Path**

- A sequence of connected activities that leads from the START node to the FINISH node.

- **Critical Path (CP)**

- One of the objectives of CPM is to determine the CP through a project network. The CP consists of the set of critical activities that if delayed in any way, would cause a delay in the completion of the entire project.

Critical Path


- **Path**

- A sequence of connected activities that leads from the START node to the FINISH node.

- **Critical Path (CP)**

- One of the objectives of CPM is to determine the CP through a project network. The CP consists of the set of critical activities that if delayed in any way, would cause a delay in the completion of the entire project.
- Clearly, critical activities are those that have **zero slack**...

CPM: Critical Path Identified

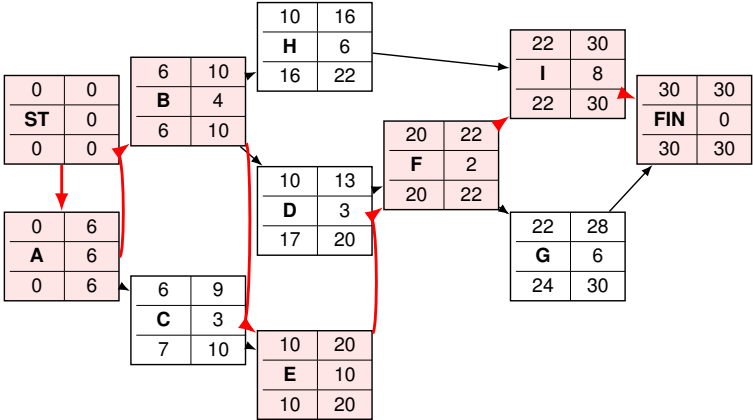

Critical Path: Start - A - B - E - F - I - Finish

Time-Cost Tradeoffs – Crashing Activities

The management of AeroTech Solutions is giving some thoughts to putting extra resources into the project so that it can be completed within **26 weeks**. Each activity has been studied, and a set of crash times (in weeks) and cost has been developed. Determine a crash plan which minimizes the total cost of completing the project within 26 weeks.

Connection to Simulation

When you decide to authorize overtime, hire more staff, or outsource to hit a looming deadline, you are effectively “**crashing**” the project. You must weigh the **cost per week saved**.

Activity	Activity Description	Normal Time	Normal Cost	Crash Time	Crash Cost
A	Conduct market analysis	6	\$240,000	5	\$300,000
B	Secure manufacturing facilities	4	\$300,000	3	\$400,000
C	Hire production managers	3	\$150,000	2	\$240,000
D	Procure raw materials	3	\$540,000	2	\$750,000

A Heuristic Approach

What activities to crash and how much to crash?

Act.	Time (T_i)	Budgeted Cost (C_i)	Crash Cost (C'_i)	Δ Cost ($C'_i - C_i$)	Δ Time ($T_i - T'_i$)	Crash Cost / Wk ($\Delta C / \Delta T$)	Slack (From CPM)
A	6	\$240,000	\$300,000	\$60,000	1	\$60,000	0
B	4	\$300,000	\$400,000	\$100,000	1	\$100,000	0
C	3	\$150,000	\$240,000	\$90,000	1	\$90,000	1
D	3	\$540,000	\$750,000	\$210,000	1	\$210,000	7
E	10	\$900,000	\$1,440,000	\$540,000	3	\$180,000	0
F	2	\$300,000	\$390,000	\$90,000	1	\$90,000	0
G	6	\$1,350,000	\$3,200,000	\$1,850,000	2	\$925,000	2
H	6	\$450,000	\$900,000	\$450,000	3	\$150,000	6
I	8	\$1,050,000	\$2,600,000	\$1,550,000	4	\$387,500	0

Current Critical Path: A - B - E - F - I (30 weeks)


Need completion in 26 weeks.

Crashing Step 1: Crash Activity A by 1 Week

- Activity A is on the critical path and has the lowest Crash Cost / Week (\$60,000).
- New Duration for A = 5.
- Entire project duration drops to **29 weeks**.

Next: Which activity to crash next?

- Check critical path. It remains **A-B-E-F-I**.
- Next cheapest on CP is F (\$90k/wk).

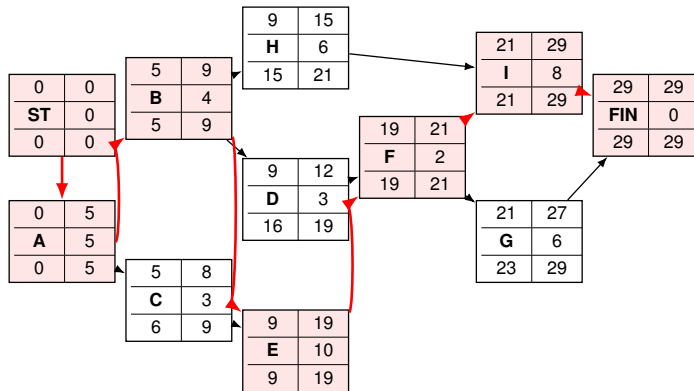


Crashing Step 2: Crash Activity F by 1 Week

- Crash F by 1 week. Cost = \$90,000.
- New Duration for F = 1.
- Entire project duration drops to **28 weeks**.

Next: Which activity to crash next?

- Check critical path. It remains **A-B-E-F-I**.
- Next cheapest on CP is B (\$100k/wk).

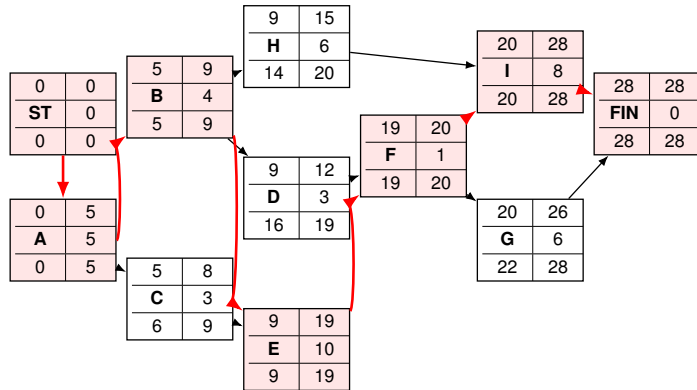


Crashing Step 3: Crash Activity B by 1 Week

- Crash B by 1 week. Cost = \$100,000.
- New Duration for B = 3.
- Entire project duration drops to **27 weeks**.


Next: Which activity to crash next?

- Check critical path. It is STILL A-B-E-F-I.
- But wait, Activity C's slack has dropped to 0!
- We now have **two** critical paths: **A-B-E-F-I** and **A-C-E-F-I**.

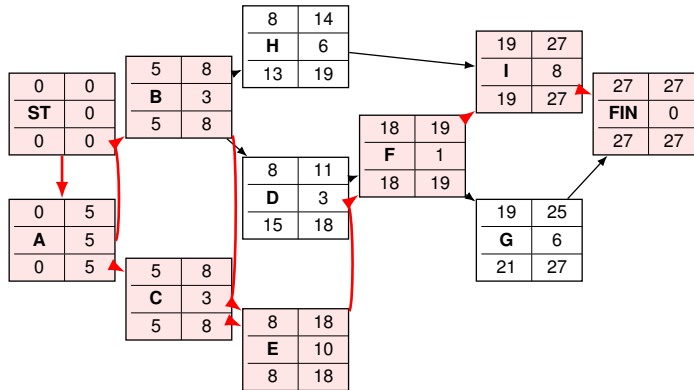


Crashing Step 4: What if we crash C?

- If we crash C (cost \$90,000/wk)...
- **Doesn't help.** Because activity E cannot start until *both* B and C finish.
- B is 3 weeks, C is 2 weeks. E still waits for B. The total duration remains 27.
- To save time, we would have to crash *both* B and C together (cost \$190,000/wk).

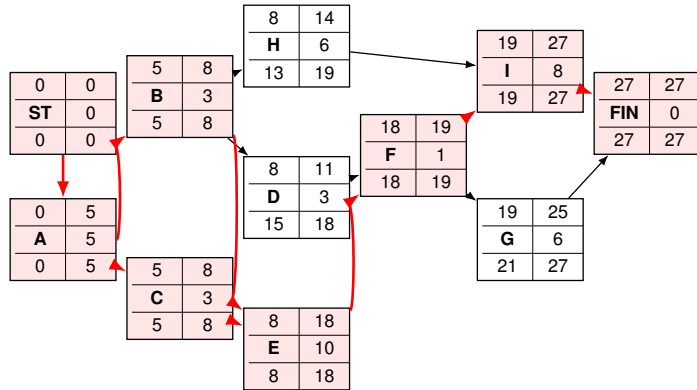

Crashing Step 5: Crash Activity E by 1 Week

- Instead of crashing B and C, crash E.
- E is on *both* critical paths!
- Crash E by 1 week. Cost = \$180,000.
- New Duration for E = 9.
- Entire project duration drops to **26 weeks!**

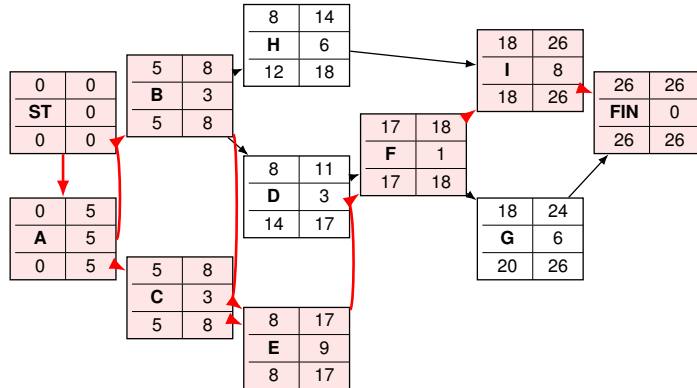

Success! We achieved 26 weeks.

About Heuristic Approach

- **Remember:**

About Heuristic Approach

- **Remember:**

- As you crash the current critical activities, other paths may become critical.

About Heuristic Approach

- **Remember:**

- As you crash the current critical activities, other paths may become critical.

- **Recommendation:**

About Heuristic Approach

- **Remember:**

- As you crash the current critical activities, other paths may become critical.

- **Recommendation:**

- Crash activities one by one.

About Heuristic Approach

- **Remember:**

- As you crash the current critical activities, other paths may become critical.

- **Recommendation:**

- Crash activities one by one.
- After crashing one activity, check the critical path(s) in the revised network.

Project Scheduling with Uncertain Activity Times

The R&D team at AeroTech used a completely new AI navigation chip for the drone. Given the massive market hype, management wants to roll out the product as soon as possible. However, due to supply chain complexities and new manufacturing techniques, the operations managers can only give a rough estimate (optimistic, most probable, pessimistic) on the duration time of activities. **What would be the expected time required to complete the project?**

Connection to Simulation

In the game, you will face unexpected curveballs (e.g., staff quitting, tech failures). PERT proves mathematically why a single deterministic plan is an illusion, and why you must manage risk dynamically.

Activity	Optimistic (a_i)	Most Probable (m_i)	Pessimistic (b_i)
A	4	6	7
B	4	6	9
...	...	...	

Three-Point Estimation Technique (PERT)

A. Time estimates

- ① For each activity, estimate:
 - a_i = optimistic time
 - b_i = pessimistic time
 - m_i = most probable time
- ② Compute approximate value assuming a beta probability distribution:

$$\text{Expected Time} = \mu_i = \frac{a_i + 4m_i + b_i}{6}$$

$$\text{Variance} = \sigma_i^2 = \left(\frac{b_i - a_i}{6} \right)^2$$

Critical Path & Probabilistic Analysis

B. Procedure


- 1 Treat the expected activity times as the known duration of activity. Use the PERT/CPM procedure to find the critical path of the project.
- 2 Compute estimates of mean and variance of project completion time as sum of expected times and variances along critical path:
 - Mean (μ) = Sum of Expected Times on Critical Path
 - Variance (σ^2) = Sum of Variances on Critical Path
- 3 Assume the project completion time is normally distributed $N(\mu, \sigma)$
- 4 Use Standardized Normal Distribution Table to determine certainty of completing project within a given time frame.

AeroTech PERT Calculations

	Activity	Optimistic	Most Prob.	Pessimistic	Mean Time (μ_i)	Variance (σ_i^2)
✓	A	4	6	7	5.83	0.25
✓	B	4	6	9	6.17	0.69
	C	3	4	5	4	0.11
	D	3	5	7	5	0.44
✓	E	10	14	16	13.67	1
✓	F	2	2	3	2.17	0.03
✓	G	6	8	12	8.33	1
	H	4	6	7	5.83	0.25
	I	6	8	9	7.83	0.25

CPM gives Critical Path: A-B-E-F-G

PERT Network Diagram (Expected Times)

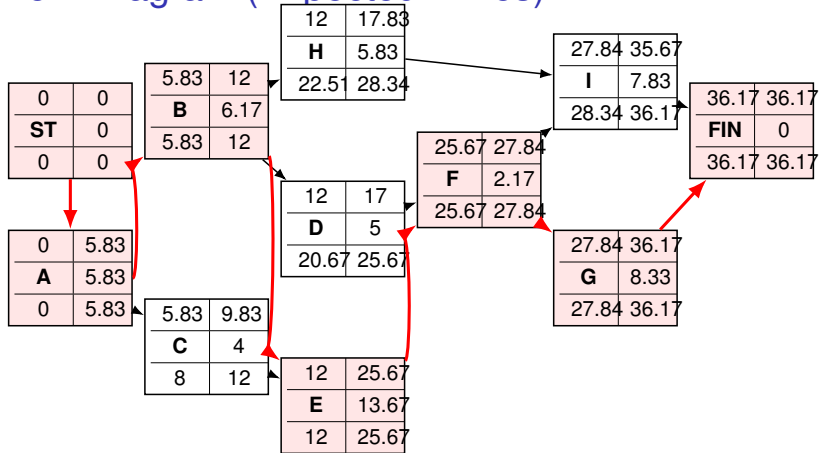

Critical Path: Start - A - B - E - F - G - Finish

Project Completion Probabilities

Suppose the critical path is: A - B - E - F - G

(1) What is the estimated expected completion time?

- $\mu_{CP} = 5.83 + 6.17 + 13.67 + 2.17 + 8.33 = 36.17$
- $\sigma_{CP}^2 = 0.25 + 0.69 + 1 + 0.03 + 1 = 2.97$

(2) What is the probability of completing the project in 33 weeks?

- $\text{NORM.DIST}(33, 36.17, \text{SQRT}(2.97), 1) = 0.0329$ or 3.3%

(3) With 90% probability, what is the project completion time?

- $\text{NORM.INV}(0.9, 36.17, \text{SQRT}(2.97)) = 38.37$ days

Putting Theory into Practice: HBS Simulation

- **The Setup:** You will step into the role of a Project Manager mid-flight.

Putting Theory into Practice: HBS Simulation

- **The Setup:** You will step into the role of a Project Manager mid-flight.
- **The Goal:** Successfully deliver a competitive product to market in a dynamic, unpredictable environment.

Putting Theory into Practice: HBS Simulation

- **The Setup:** You will step into the role of a Project Manager mid-flight.
- **The Goal:** Successfully deliver a competitive product to market in a dynamic, unpredictable environment.
- **The 3 Levers:** Manage **Scope** dynamically, allocate **Resources** wisely, and hit **Schedule** deadlines.

Putting Theory into Practice: HBS Simulation

- **The Setup:** You will step into the role of a Project Manager mid-flight.
- **The Goal:** Successfully deliver a competitive product to market in a dynamic, unpredictable environment.
- **The 3 Levers:** Manage **Scope** dynamically, allocate **Resources** wisely, and hit **Schedule** deadlines.
- **The Human Element:** You must also manage team morale, stress, and coordination meetings (standups, coaching).

Scenario A: Realistic Targets

- **The Situation:** A standard project with realistic targets and relatively low uncertainty.

Scenario A: Realistic Targets

- **The Situation:** A standard project with realistic targets and relatively low uncertainty.
- **Your Strategy:**

Scenario A: Realistic Targets

- **The Situation:** A standard project with realistic targets and relatively low uncertainty.
- **Your Strategy:**
 - What resource choices (team size, skill, overtime, outsourcing) give you the best results?

Scenario A: Realistic Targets

- **The Situation:** A standard project with realistic targets and relatively low uncertainty.
- **Your Strategy:**
 - What resource choices (team size, skill, overtime, outsourcing) give you the best results?
 - Do you need prototypes? Why or why not?

Scenario A: Realistic Targets

- **The Situation:** A standard project with realistic targets and relatively low uncertainty.
- **Your Strategy:**
 - What resource choices (team size, skill, overtime, outsourcing) give you the best results?
 - Do you need prototypes? Why or why not?
 - Will you ever delay non-critical tasks?

Scenario A: Realistic Targets

- **The Situation:** A standard project with realistic targets and relatively low uncertainty.
- **Your Strategy:**
 - What resource choices (team size, skill, overtime, outsourcing) give you the best results?
 - Do you need prototypes? Why or why not?
 - Will you ever delay non-critical tasks?
- **Apply the Class Tools:** How can identifying **slack** from CPM help you optimize resources in this scenario?

Scenario C: Mid-Project Surprise

- **The Situation:** A competitor issues a surprise announcement mid-project, abruptly tightening your schedule target.

Scenario C: Mid-Project Surprise

- **The Situation:** A competitor issues a surprise announcement mid-project, abruptly tightening your schedule target.
- **Your Strategy:**

Scenario C: Mid-Project Surprise

- **The Situation:** A competitor issues a surprise announcement mid-project, abruptly tightening your schedule target.
- **Your Strategy:**
 - When the schedule suddenly shrinks, what do you do? Add resources? Cut scope? Authorize more overtime?

Scenario C: Mid-Project Surprise

- **The Situation:** A competitor issues a surprise announcement mid-project, abruptly tightening your schedule target.
- **Your Strategy:**
 - When the schedule suddenly shrinks, what do you do? Add resources? Cut scope? Authorize more overtime?
 - What happens to team morale and product quality?

Scenario C: Mid-Project Surprise

- **The Situation:** A competitor issues a surprise announcement mid-project, abruptly tightening your schedule target.
- **Your Strategy:**
 - When the schedule suddenly shrinks, what do you do? Add resources? Cut scope? Authorize more overtime?
 - What happens to team morale and product quality?
- **Apply the Class Tools:** How is this like **crashing** activities after you have already started the project? Did any new activities suddenly become critical?

Connecting the Simulation to Session 3 Tools

As you play, keep these three analytical tools in mind:

- 1 **CPM & Critical Path:** Did the critical path change when you made decisions or when surprises occurred?

Connecting the Simulation to Session 3 Tools

As you play, keep these three analytical tools in mind:

- 1 **CPM & Critical Path:** Did the critical path change when you made decisions or when surprises occurred?
- 2 **Crashing:** Did adding resources always save time? Or were there hidden costs (Brooks's Law, communication overhead)?

Connecting the Simulation to Session 3 Tools

As you play, keep these three analytical tools in mind:

- 1 **CPM & Critical Path:** Did the critical path change when you made decisions or when surprises occurred?
- 2 **Crashing:** Did adding resources always save time? Or were there hidden costs (Brooks's Law, communication overhead)?
- 3 **PERT / Uncertainty:** How did the surprises in Scenario C feel compared to the mathematical variance (σ^2) in our PERT activity times?

Connecting the Simulation to Session 3 Tools

As you play, keep these three analytical tools in mind:

- 1 **CPM & Critical Path:** Did the critical path change when you made decisions or when surprises occurred?
- 2 **Crashing:** Did adding resources always save time? Or were there hidden costs (Brooks's Law, communication overhead)?
- 3 **PERT / Uncertainty:** How did the surprises in Scenario C feel compared to the mathematical variance (σ^2) in our PERT activity times?

Connecting the Simulation to Session 3 Tools

As you play, keep these three analytical tools in mind:

- 1 **CPM & Critical Path:** Did the critical path change when you made decisions or when surprises occurred?
- 2 **Crashing:** Did adding resources always save time? Or were there hidden costs (Brooks's Law, communication overhead)?
- 3 **PERT / Uncertainty:** How did the surprises in Scenario C feel compared to the mathematical variance (σ^2) in our PERT activity times?

Let's log in and play!
